BC CONSTRUCTION EMPLOYERS BUILDING RELATIONSHIPS
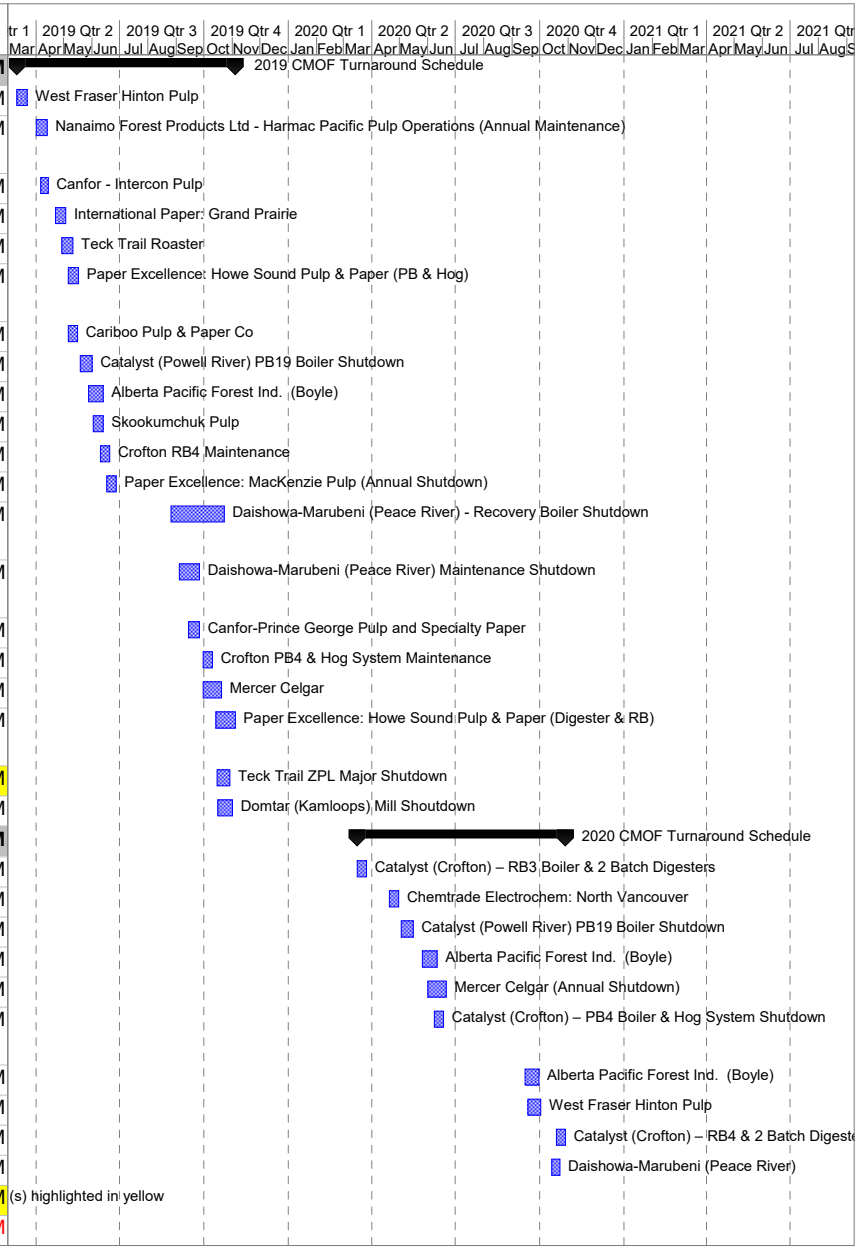
ID	Task Name	% Compl	Total Contract	Boil Mkr (T2)	Duration	Feed Off	Feed On
1	**2019 CMOF Turnaround Schedule**	**0%**			**238 days**	**Mar 11 7:00 AM**	**Nov 04 7:00 AM**
2	West Fraser Hinton Pulp	0%			11 days	Mar 11 7:00 AM	Mar 22 7:00 AM
3	Nanaimo Forest Products Ltd - Harmac Pacific Pulp Operations (Annual Maintenance)	0%	600		12 days	Apr 01 7:00 AM	Apr 13 7:00 AM
4	Canfor - Intercon Pulp	0%			8 days	Apr 06 7:00 AM	Apr 14 7:00 AM
5	International Paper: Grand Prairie	0%			11 days	Apr 22 7:00 AM	May 03 7:00 AM
6	Teck Trail Roaster	0%	250	50	12 days	Apr 29 7:00 AM	May 11 7:00 AM
7	Paper Excellence: Howe Sound Pulp & Paper (PB & Hog)	0%	200		11 days	May 06 7:00 AM	May 17 7:00 AM
8	Cariboo Pulp & Paper Co	0%	1200	300	10 days	May 06 7:00 AM	May 16 7:00 AM
9	Catalyst (Powell River) PB19 Boiler Shutdown	0%		70	13 days	May 19 7:00 AM	Jun 01 7:00 AM
10	Alberta Pacific Forest Ind. (Boyle)	0%			16 days	May 28 7:00 AM	Jun 13 7:00 AM
11	Skookumchuk Pulp	0%			11 days	Jun 02 7:00 AM	Jun 13 7:00 AM
12	Crofton RB4 Maintenance	0%	400	100	10 days	Jun 10 7:00 AM	Jun 20 7:00 AM
13	Paper Excellence: MacKenzie Pulp (Annual Shutd	0%			10 days	Jun 17 7:00 AM	Jun 27 7:00 AM
14	Daishowa-Marubeni (Peace River) - Recovery Boiler Shutdown	0%			58 days	Aug 26 7:00 AM	Oct 23 7:00 AM
15	Daishowa-Marubeni (Peace River) Maintenance Shutdown	0%			22 days	Sep 04 7:00 AM	Sep 26 7:00 AM
16	Canfor-Prince George Pulp and Specialty Paper	0%			12 days	Sep 14 7:00 AM	Sep 26 7:00 AM
17	Crofton PB4 & Hog System Maintenance	0%	200	100	10 days	Sep 30 7:00 AM	Oct 10 7:00 AM
18	Mercer Celgar	0%			20 days	Sep 30 7:00 AM	Oct 20 7:00 AM
19	Paper Excellence: Howe Sound Pulp & Paper (Digester & RB)	0%	650		21 days	Oct 14 7:00 AM	Nov 04 7:00 AM
20	Teck Trail ZPL Major Shutdown	0%	150	25	14 days	Oct 15 7:00 AM	Oct 29 7:00 AM
21	Domtar (Kamloops) Mill Shoutdown	0%			16 days	Oct 16 7:00 AM	Nov 01 7:00 AM
22	**2020 CMOF Turnaround Schedule**	**0%**			**227 days**	**Mar 16 7:00 AM**	**Oct 29 7:00 AM**
23	Catalyst (Crofton) – RB3 Boiler & 2 Batch Digester	0%	400	100	10 days	Mar 16 7:00 AM	Mar 26 7:00 AM
24	Chemtrade Electrochem: North Vancouver	0%			10 days	Apr 20 7:00 AM	Apr 30 7:00 AM
25	Catalyst (Powell River) PB19 Boiler Shutdown	0%		50	13 days	May 03 7:00 AM	May 16 7:00 AM
26	Alberta Pacific Forest Ind. (Boyle)	0%			16 days	May 26 7:00 AM	Jun 11 7:00 AM
27	Mercer Celgar (Annual Shutdown)	0%			20 days	Jun 01 7:00 AM	Jun 21 7:00 AM
28	Catalyst (Crofton) – PB4 Boiler & Hog System Shutdown	0%	200	100	10 days	Jun 08 7:00 AM	Jun 18 7:00 AM
29	Alberta Pacific Forest Ind. (Boyle)	0%			15 days	Sep 15 7:00 AM	Sep 30 7:00 AM
30	West Fraser Hinton Pulp	0%			14 days	Sep 18 7:00 AM	Oct 02 7:00 AM
31	Catalyst (Crofton) – RB4 & 2 Batch Digesters	0%	400	100	10 days	Oct 19 7:00 AM	Oct 29 7:00 AM
32	Daishowa-Marubeni (Peace River)	0%			9 days	Oct 14 7:00 AM	Oct 23 7:00 AM
33	Change(s) highlighted in yellow	0%			0 days	Dec 18 7:00 AM	Dec 18 7:00 AM
34	Rev. Dec 18, 2018	0%			0 days	Dec 18 7:00 AM	Dec 18 7:00 AM
